June 2, 2016

UPDATED AUGUST 10, 2016

TOWN OF BOURNE, MASSACHUSETTS

PEEBLES ELEMENTARY SCHOOL

PROJECT SCHEDULE

PROJECT MANAGEMENT SMMA

2016 SPECIAL TOWN MEETING AND SPECIAL ELECTION BALLOT VOTE
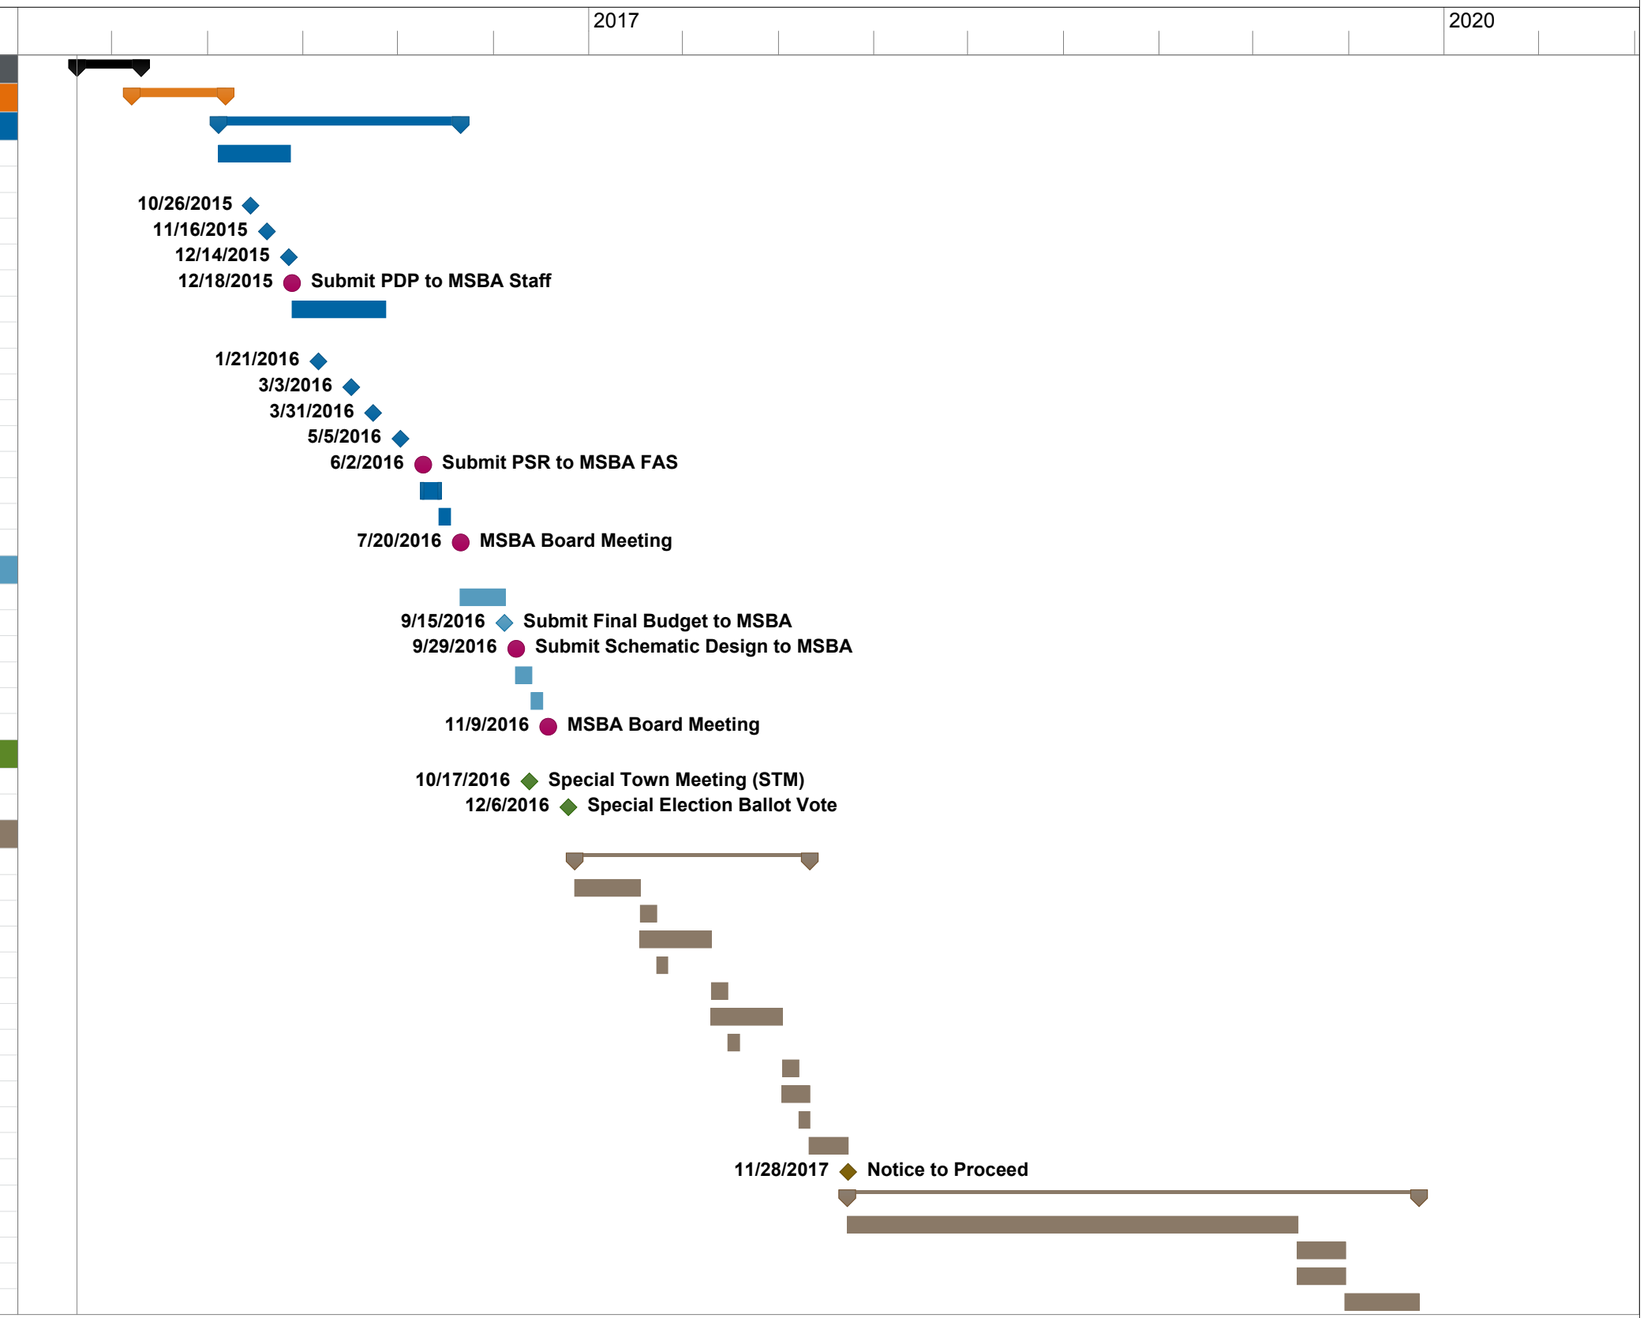
ID	Task Name	Duration	Start	Finish
1	**RETAIN OPM**	**58 days**	**3/18/2015**	**6/8/2015**
7	**RETAIN DESIGNER**	**85 days**	**5/27/2015**	**9/23/2015**
17	**FEASIBILITY STUDY (FS)**	**218 days**	**9/15/2015**	**7/20/2016**
18	Develop Preliminary Design Program (PDP)	65 days	9/15/2015	12/15/2015
19	**Community Presentations**	34 days	10/26/2015	12/14/2015
20	Community Forum 1	0 days	10/26/2015	10/26/2015
21	Community Forum 2	0 days	11/16/2015	11/16/2015
22	Community Forum 3	0 days	12/14/2015	12/14/2015
23	**Submit PDP to MSBA Staff**	**0 days**	**12/18/2015**	**12/18/2015**
24	Develop Preferred Schematic Report (PSR)	84 days	12/18/2015	4/15/2016
25	**Community Presentations**	75 days	1/21/2016	5/5/2016
26	Community Forum 4	0 days	1/21/2016	1/21/2016
27	Community Forum 5	0 days	3/3/2016	3/3/2016
28	Community Forum 6	0 days	3/31/2016	3/31/2016
29	Community Forum 7	0 days	5/5/2016	5/5/2016
30	**Submit PSR to MSBA FAS**	**0 days**	**6/2/2016**	**6/2/2016**
31	MSBA Comments	16 days	6/2/2016	6/23/2016
32	Respond to MSBA Comments	10 days	6/23/2016	7/7/2016
33	**MSBA Board Meeting**	**0 days**	**7/20/2016**	**7/20/2016**
34	**SCHEMATIC DESIGN (SD)**	**80 days**	**7/20/2016**	**11/9/2016**
35	Develop Schematic Design	41 days	7/20/2016	9/15/2016
36	Submit Final Budget to MSBA	0 days	9/15/2016	9/15/2016
37	**Submit Schematic Design to MSBA**	**0 days**	**9/29/2016**	**9/29/2016**
38	MSBA Comments	15 days	9/29/2016	10/19/2016
39	Respond to MSBA Comments	11 days	10/19/2016	11/2/2016
40	**MSBA Board Meeting**	**0 days**	**11/9/2016**	**11/9/2016**
41	**LOCAL VOTES**	**35 days**	**10/17/2016**	**12/6/2016**
42	Special Town Meeting (STM)	0 days	10/17/2016	10/17/2016
43	Special Election Ballot Vote	0 days	12/6/2016	12/6/2016
44	**DESIGN AND CONSTRUCTION**	**760 days**	**12/14/2016**	**11/29/2019**
45	**Design and Documentation**	**213 days**	**12/14/2016**	**10/10/2017**
46	Design Development	60 days	12/14/2016	3/7/2017
47	MSBA Review	15 days	3/8/2017	3/28/2017
48	60% Construction Documents	66 days	3/7/2017	6/6/2017
49	Incorporate MSBA DD Comments	10 days	3/29/2017	4/11/2017
50	MSBA Review	15 days	6/7/2017	6/27/2017
51	90% Construction Documents	64 days	6/6/2017	9/5/2017
52	Incorporate MSBA 60% CD Comments	10 days	6/28/2017	7/12/2017
53	MSBA Review	15 days	9/6/2017	9/26/2017
54	100% Construction Documents	26 days	9/5/2017	10/10/2017
55	Incorporate MSBA 90% CD Comments	10 days	9/27/2017	10/10/2017
56	**Bidding and Award**	**36 days**	**10/10/2017**	**11/28/2017**
57	**Notice to Proceed**	**0 days**	**11/28/2017**	**11/28/2017**
58	**Construction**	**513 days**	**11/28/2017**	**11/29/2019**
59	Building Substantial Completion	405 days	11/28/2017	6/27/2019
60	Move-In	43 days	6/27/2019	8/27/2019
61	Demolition of Existing Building	43 days	6/27/2019	8/27/2019
62	Final Sitework	67 days	8/27/2019	11/29/2019
